

August 27, 2019

Membership	Meeting Schedule
 Community Members Bryan ISD Board Members Parents School Administrators District Leaders (Ad Hoc) 	 June 25, 2019 September 24, 2019 January 14, 2020 March 24, 2020 June 9, 2020 September 22, 2020 December 8, 2020

Purpose of the Committee

- Work in an advisory capacity with Bryan ISD Administration.
- Review the status of capital projects, bond expenditures, project schedules, and the timelines for construction projects.
- Confirm fidelity of the actual work and expenditures to the projects presented to and approved by the voters.
- Report status and findings to the Bryan ISD Board of Trustees on a periodic basis.

2019 Bond Projects

• Bryan High roof replacement





Roof over Gym # 2

Roof over 5200 wing

2019 Bond Projects

• Purchase of School Buses






2019 Bond Projects

• Purchase of CTE Equipment for the Bryan Career and Technical Education Complex



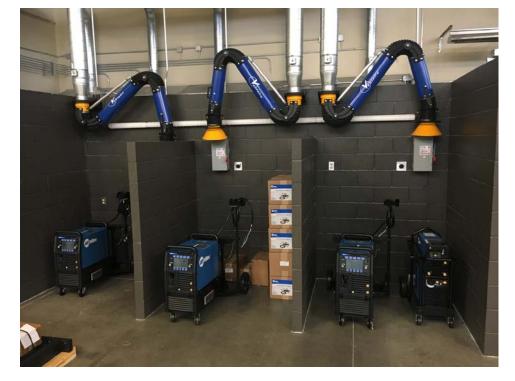

Welders, Snorkels, Welding Booths

CNC Plasma Table

Bond Construction & Financial Update:



2019 Bond Projects

• Roofing Projects - Budget \$4,193,640 (Financial Commitments = \$2,830,258)

- Bryan High School Re-Roof (\$2,240,045) Construction: May-October 2019
 - Gym #2
 - 5200 wing
 - 6100 wing
 - Built Up Roof Area
- Mary Catherine Harris Re-Roof (\$590,213) Construction: May-August 2019
- Travis Educational Support Center Re-Roof Construction: Fall/Winter 2019
- Neal Elementary Re-Roof *Construction: Summer 2020*
- Stephen F. Austin Middle School Library Re-Roof Construction: Summer 2020

• Maintenance & Operations Projects - Budget \$962,610 (Financial Commitments = \$690,016)

- Bryan High School Boiler (\$64,010) *Construction: April-June 2019*
- Bryan High School HVAC Controls Replacement (\$626,006) Construction: June-Fall 2019
- CTE Complex Equipment Budget \$1,000,000 (Financial Commitments = \$835,234)

2019 Bond Projects

- Transportation Budget \$2,800,000 (Financial Commitments = \$2,800,378)
 - School Bus Purchase, 28 total
 - Handicap Van
- Safety and Security Budget \$2,643,750
 - Security Vestibule Intrusion Resistant Film, District-Wide *Construction: July-September 2019*
 - Security Cameras, Elementary Schools specified locations
 - Key Card Access, District wide specified locations
 - Fire Panel Replacement *Construction: Fall 2019-Spring 2020*
 - Rayburn Intermediate School
 - Bryan Collegiate High School
 - Fannin Elementary

2019 Bond Projects


• Safety & Security Projects, contd.

Security Fencing Construction: September 2019-January 2020

- Houston Elementary
- Navarro Elementary
- Bowen Elementary
- Ross Elementary
- Jones Elementary
- Branch Elementary
- Mitchell Elementary
- Neal Elementary
- Henderson Elementary
- Long Intermediate School
- Rayburn Intermediate School
- Davila Middle School
- Bonham Elementary, Around Detention Pond

Financial Commitments

\$7,155,886

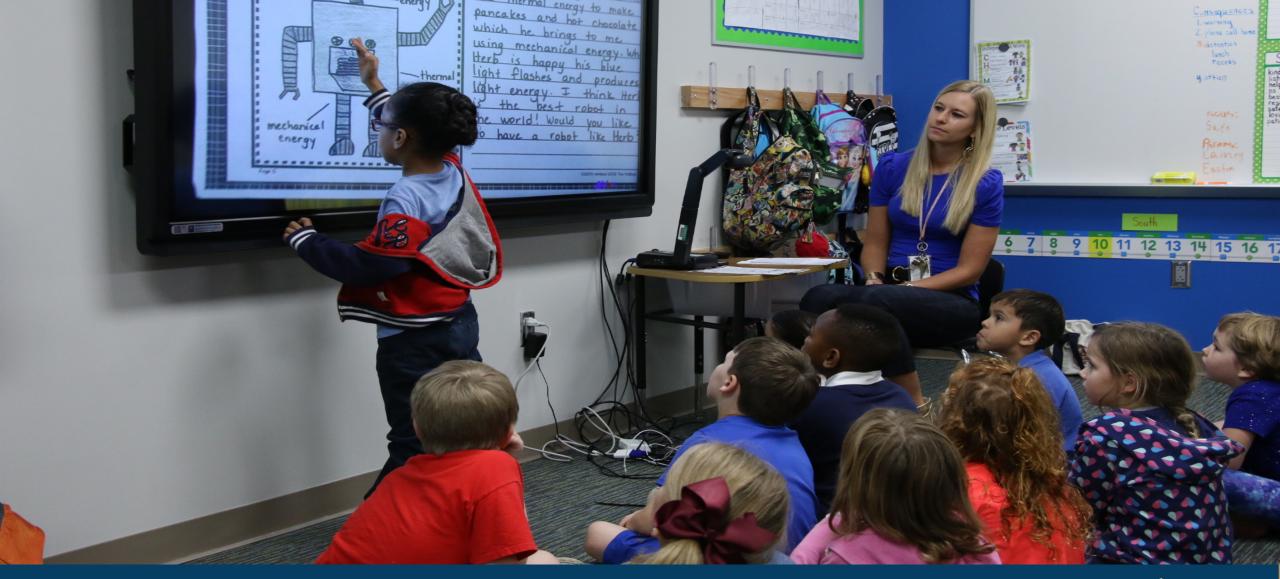

Next Steps



Bryan ISD 2020 Bond Steering Update




August 27, 2019

Committee Members & Meeting Schedule

- Students
- Parents
- Community Members
- Campus Teachers
- Campus Administrators
- Board Members
- District Leaders

- July 23, 2019
- August 13, 2019
- September 10, 2019
- September 26, 2019
- October 1, 2019
- October 22, 2019
- November 5, 2019
- November 21, 2019
- December 10, 2019

BRYAN ISD PRESENTS 2 BONDS, 1 VISION: UNLIMITED STUDENT SUCCESS



BRYANISD.ORG/BOND

Based upon studies from school facility & demographic experts, Bryan ISD's 2019 & anticipated 2020 bonds are two steps of one vision to provide students with educational facilities that will set them up for success.

Steering Committee Planning Process

ESTABLISH PRIORITIES

Facility Needs

- Capacity
- Utilization

Student Enrollment

- Current & projected
- Full day prekindergarten

DEVELOP OPTIONS

• Align needs & priorities with Vision, Mission, & Board Goals

DEVELOP RECOMMENDATIONS

- Update School Board periodically
- Present final recommendation to School Board in January, 2020

Focus & Data Sources

- High Schools
- Middle Schools
- Intermediate Schools
- Elementary Schools
- Non-Campus Facilities
- Transportation Facility

Current Enrollment

Prekindergarten EnrollmentCurrent Status

Projected Enrollment (PASA Report)

Facility Condition Assessment (PBK Report)

Financial Update

- District maintains a strong financial position
- Aggressively paid down debt
- Strong Financial Ratings on past bonds (Fitch AA) (Standard & Poor's AA-)
- Current Bonding Capacity at \$0.28 I & S Tax Rate is approximately \$125 Million
- Potential Capacity at \$0.29 (or 1 cent increase) I&S Tax Rate is approximately \$160 Million
- Recap of Law Changes in Bond Referendums
 - ■HB 3 Ballot Language
 - ■SB 30 Requires Separate Propositions for Certain Items
 - ■HB 440 Limits District's Use of Unspent Bond Proceeds
 - ■HB 477 Ballot Language and Voter Information

Preliminary Bond Priority Interests

Campus Facilities			N
Considerable Interest			C
	Create a third Intermediate School.		ŀ
	Reduce portable buildings by adding classrooms as applicable.	-	С /
	Renovate SFA Middle School Annex.		C
	Address level 1-2 priorities in the facility condition assessment. (PBK report)		

Non-Campus Facilities

Considerable Interest

Address the needs of the transportation department.

Address level 1-2 priorities in the facility condition assessment. (PBK report)



Next Steps
