
## CAPITAL PROJECTS UPDATE

November 9, 2023





### **CURRENT CAPITAL PROJECTS**

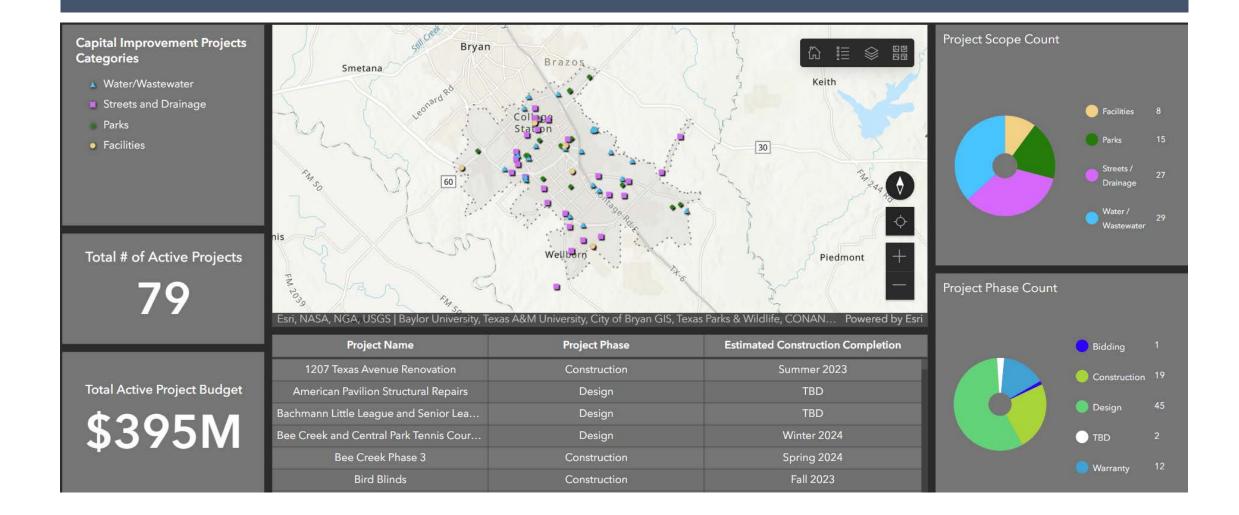




### **BOND PROJECTS**

2022

Bond

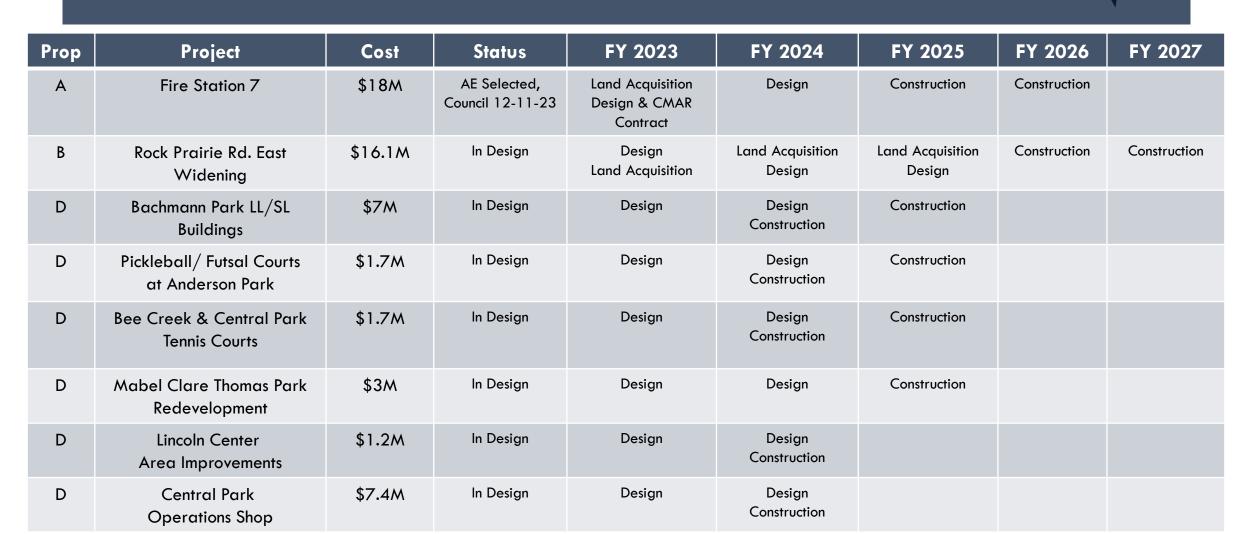



### GREENS PRAIRIE WIDENING FROM DALTON (CITY LIMITS) TO ARRINGTON RD

### Scope

Widen the previous 2-lane road to a 4-lane minor arterial with medians and improved pedestrian facilities. Installation of a traffic signal at Castlegate Drive.


Budget

\$10.7M (Design & Construction)

### Update

Construction is 95% complete

Schedule Estimated completion end of 2023

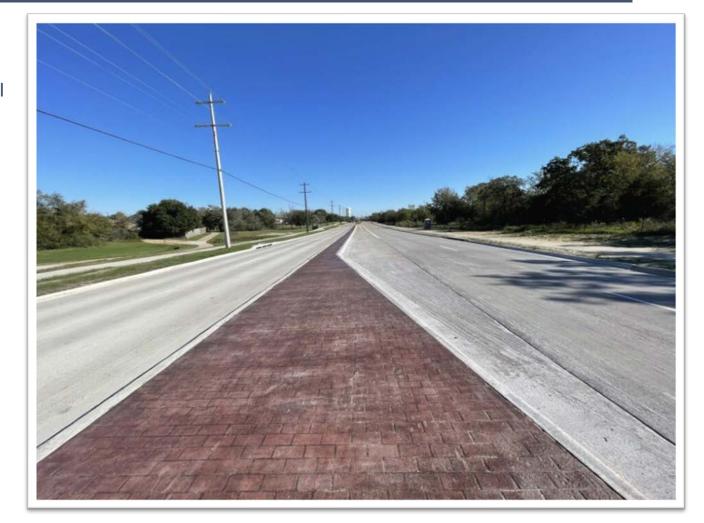



### **DEACON/CAIN RAILROAD CROSSING**

### Scope

Closure of the rail crossing at Cain Road to improve vehicular and pedestrian safety. Opening of a new rail crossing at Deacon Dr. with a signalized intersection at Deacon and Wellborn Rd. This project required raising Wellborn Rd to meet the adjacent grade required to enable Deacon Dr. to cross the adjacent railroad tracks.

#### **Budget**

\$8M (Design & Construction)

#### Update

Construction is 95% complete

### Schedule

Estimated early 2024 construction completion (dependent on weather and UPRR coordination)






### **GEORGE BUSH SEPARATED BIKE LANES**

### Scope

Construct on-street, separated bike lanes on George Bush Drive from Wellborn Road to Texas Avenue. Scope also includes applicable intersection, driveway, and sidewalk improvements.

### **Budget**

Awarded \$1M construction funding through TASA (Transportation Alternative Set-Aside) grant from the Texas Department of Transportation (TxDOT). The City of College Station has a \$750,000 budget for the design cost and is responsible for 20% of construction costs, as required by the TASA grant.

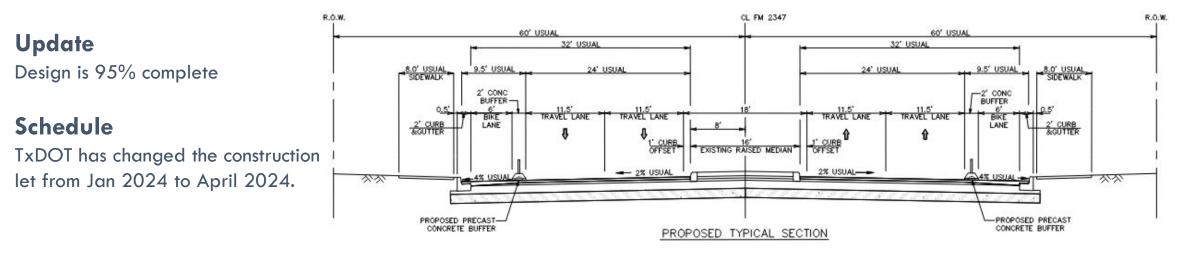



### **KRENEK TAP REHABILITATION**

### Scope

Approximately 6,000 linear feet of new concrete pavement including 10' wide sidewalks and replacing existing storm and sanitary sewer.

#### **Budget**

\$5.25M (Design & Construction)

**Update** Currently working on 90% plans

**Schedule** Construction completion anticipated Fall 2025





### **LUTHER STREET REHAB**

### Scope

The project includes the construction of approximately1,500 linear feet of improvements of Luther St. from Marion Pugh Blvd to Penberthy Blvd. These improvements consist of removal and replacement of the existing roadway pavement, addition of sidewalk, installation of a storm drain system, and replacement of the existing16-inch water main.

#### **Budget**

\$3.6M (Design & Construction)

#### Update

Staff Recommendation of Construction Contract to Council on November 9, 2023

#### Schedule

Construction completion anticipated late 2024





### VICTORIA AVENUE ROUNDABOUTS

### Scope

Construct roundabouts at Victoria/Woodlake and Victoria/Creek Meadows intersections.

#### **Budget**


\$4.3M (Design & Construction)

### Update

60% plans complete, working on easements, public meeting held in September.

### Schedule

Anticipated construction start late 2024/early 2025 (depending on easements, school schedule, and utility coordination).

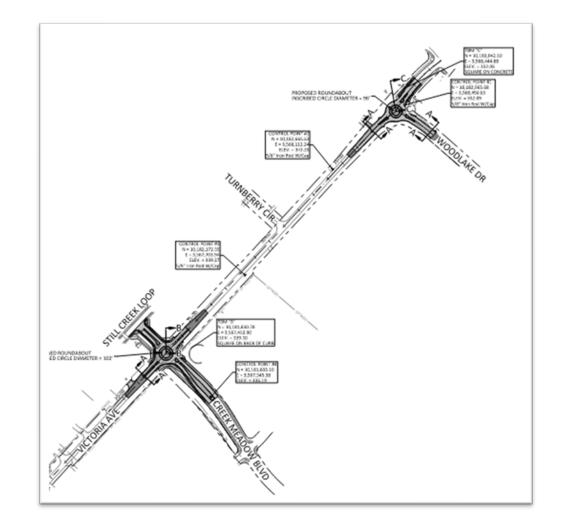



### **BEE CREEK TRUNKLINE PHASE III**

### Scope

Approximately 4,100 lf of 48-inch & 1,750 lf of 42-inch fiberglass (FRP) sewer pipe along Bee Creek between SH6 and Longmire Ct. The project will also include approximately 3,200 LF of cast in place pipe.

#### **Budget**

\$5.3M (Design & Construction)

### Update

The project is currently under construction between SH 6 and Dartmouth.

### Schedule

Construction began September 2023 and is expected to be completed in Fall 2024.





### HOLLEMAN DRIVE WEST / JONES BUTLER ROAD ROUNDABOUT

### Scope

Design and construction of a new roundabout to replace the existing four way stop at the Holleman Dr. West and Jones Butler Rd. intersection. Design and construction of the new sidewalk will include cyclist and pedestrian shared use pathways that will connect to existing sidewalks. Additionally, new ADA ramps will be added at the pedestrian crossing locations.

#### **Budget**

\$1.2M (Design & Construction)

### Update

Project will follow Luther Rehab Project construction

Schedule

Construction completion anticipated spring 2026






### LINCOLN AVENUE REHAB

### Scope

This project includes reconstruction of Lincoln Avenue from Texas Ave to University Dr. The existing asphalt will be replaced with concrete pavement and a shared use path. The project replaces water and wastewater utilities, and underground storm sewer as well as a signal modification at the University Dr. with a designated right turn lane. Roundabouts will be added at the Munson Ave. and Nimitz St. intersections.

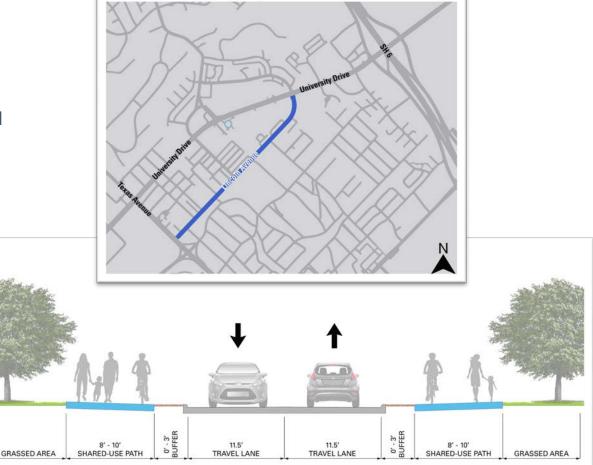

### Budget

\$10.3M (Design & Construction)

#### Update

Will Bid via Competitive Sealed Proposals November 2023

### Schedule

Construction completion anticipated late 2025.

### **Proposed Typical Section**



### **MARION PUGH DRIVE REHAB**

### Scope

This project includes the reconstruction of Marion Pugh Drive from Luther Street to George Bush Drive. The design will include a 3-lane concrete section with bike lanes, storm sewer, and two 6-ft sidewalks back of curb. The project also includes replacing approximately 3,500 the existing RCP 18" water line along Marion Pugh Drive between George Bush Drive and Holleman Drive with a new 24" water line. Demolishing/permanent abandonment of

inactive Wellborn Interconnect.

#### Budget

\$6.5M (Design & Construction)

#### Update

Project is in design, 30% Conceptual Plan Set is due April 2024.

### Schedule

Construction completion anticipated Fall 2026





### ROCK PRAIRIE ROAD WEST WIDENING (WELLBORN RD TO CITY LIMITS)

### Scope

Reconstruction of Rock Prairie Road West from Wellborn Road to the west city limits. Existing asphalt road will be replaced with concrete roadway with curb & gutter, underground storm sewer and sidewalks. Adjustments will be made to the railroad crossing.

#### **Budget**

\$7.41M (Design & Construction)



### Update

Signals are being installed at intersection of Wellborn Road and Rock Prairie Road. New signals will not go live until the intersection at Deacon is complete due to coordination required with Union Pacific Railroad.

### Schedule

Construction completion anticipated Spring 2024, pending UPRR coordination.



### ROCK PRAIRIE ROAD WIDENING (STATE HWY 6 TO TOWN LAKE)

#### Scope

Reconstruction of Rock Prairie Road will approximately extend from State Highway 6 to Town Lake. The existing asphalt road will be replaced with concrete roadway with curb & gutter, underground storm sewer, bike paths, and sidewalks.

#### **Budget**

\$8.55M (Design & Construction)

### Update

Construction will begin December 2023

### Schedule

Construction completion anticipated late 2025.







### ROCK PRAIRIE EAST WIDENING (TOWN LAKE TO WD FITCH)

### Scope

Widening of Rock Prairie east corridor from Town Lake to William D. Fitch PKWY from a two-lane asphalt roadway to four-lane concrete roadway with separated bike lanes and sidewalks adjacent to each side. Additional work includes storm sewer, street lighting, and a traffic signal at Town Lake.


#### **Budget**

\$16.1M (Design & Construction)

**Update** 30% design submittal due February 2024

#### Schedule

Anticipating substantial completion Fall 2027

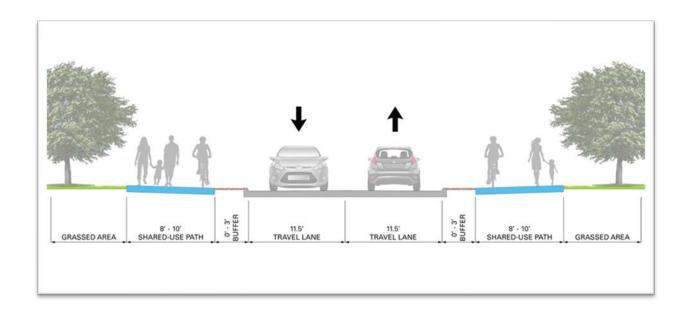

2022 Bond



# ORAINAGE IMPROVEMENTS OUNIVERSITY OAKS AND STALLINGS

### Scope

Removal and replacement of the existing culverts and pavement, additional inlets and storm sewer to tie in the existing system for one proposed discharge point.

#### **Budget**

\$ 975k (Design & Construction)

### Update

Culverts have been installed and backfilled. Work is continuing on the rest of the storm sewer pipe and water line improvements.

### Schedule

Construction to be complete Spring 2024.





### **MCCULLOCH UTILITY REHAB**

### Scope

Rehabilitation of water and wastewater lines in the Southgate area, in the vicinity of Arizona Street, Phoenix Street, Carolina Street, and Georgia Street. The wastewater lines need replacement due to an increase in service disruptions caused by shallow, deteriorating lines and poor access to mains located near back lot lines.

The water distribution lines need replacement due to an increase in service disruptions caused by deteriorating lines and inadequate fire protection as a result of small line sizes in the system.

#### **Budget**

\$7.4M (Design & Construction)

### Update

Bid early 2024, pending TxDOT Permit.

**Schedule** Construction start anticipated in Spring/Summer 2024





### **COLLEGE HEIGHTS UTILITY REHAB**

### Scope

Replacement and/or rehab of approximately 13,080 lf of existing waterlines and 6,600 lf of wastewater lines in the College Heights area as shown on the image.

#### **Budget**


\$5.74M (Design & Construction)

Update

Project is in design. Conceptual design due January 2024.

### Schedule

Construction anticipated to begin in 2025

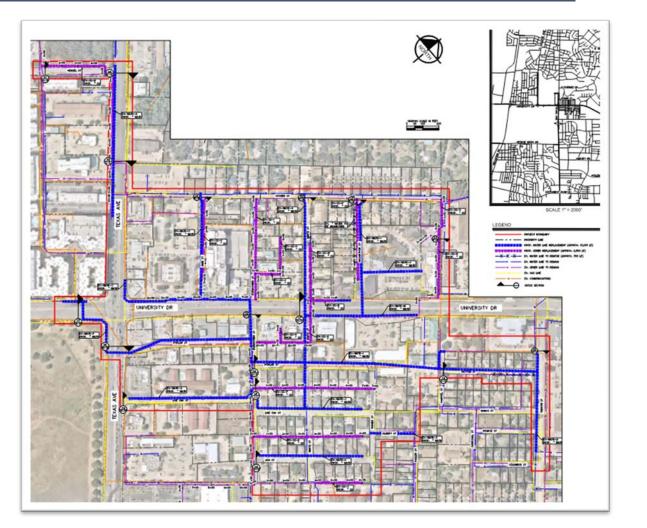



### FUEL STATION AT ARNOLD ROAD

#### Scope

Construction of a new Fuel Station at Arnold Road. In addition, the project includes pump mechanisms, card readers, and software upgrades to ensure compliance with Texas Commission on Environment Quality and Code of Federal Regulations.

#### Budget


\$2.4M (Design & Construction)

### Update

Project is nearing completion.

### Schedule

Final completion anticipated December 2023.

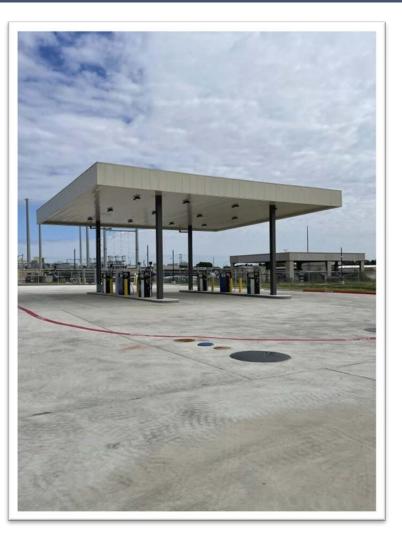



### SANDY POINT PUMP STATION SITE IMPROVEMENTS

#### Scope

Improvements to the Sandy Point Pump Station including security fencing improvements and construction of a pre-engineered metal building to protect and preserve the division's vehicles and equipment.

**Budget** \$1.45M (Design & Construction)

#### Update

Construction is at Substantial Completion

**Schedule** Final completion anticipated December 2023.





### **CSU ENTRY REMODEL**

#### Scope

Redesign entry clerestory to remove existing window system that is leaking.

### **Budget**


\$100k (Design and Construction)

### Update

Final design due December 2023

### Schedule

Construction anticipated to begin Spring 2024







### AGGIE FIELD OF HONOR CEMETERY SALES & MAINTENANCE SHOP

### Scope

Construct a new, fully secure, and functional maintenance crew shop, as well as an office/meeting area for sale of plots within the cemetery

#### **Budget**

\$2.33M (Design & Construction)

### Update

This project was completed in June of this year.







### LICK CREEK HIKE & BIKE TRAIL IMPROVEMENTS

### Scope

Demolish and raise the existing sidewalk under Midtown Drive. Construction of additional sidewalk to access Midtown Drive.

**Budget** \$450,000 (Design & Construction)

**Update** Substantial completion October 2023

### Schedule

Contractor working on repairing items not accepted by the City. Work to be completed by December.





### SOUTHEAST PARK

#### Scope

Gathering public input regarding future baseball fields and a future SE Park located on Rock Prairie Road.

### Update

Surveys are live and two public meetings have been held.





### BEE CREEK AND CENTRAL PARK TENNIS COURTS IMPROVEMENTS



### Scope

Project will reconstruct the Bee Creek Park and Central Park Tennis Courts with new playing surfaces, court lighting, fencing, netting and windscreens.

### **Budget**

\$1.7M

### Update

Public meeting held in October, progressing towards 60% design

### Schedule

Construction anticipated to be completed in late 2024





### BACHMANN PARK SENIOR AND LITTLE LEAGUE BUILDINGS



### Scope

Demolition and re-construction of both the Senior league and Little League restroom and concession buildings.

### Budget


\$7M

### Update

50% drawings submitted and are under review by various City Departments.

### Schedule

Estimated construction to start in 2024.

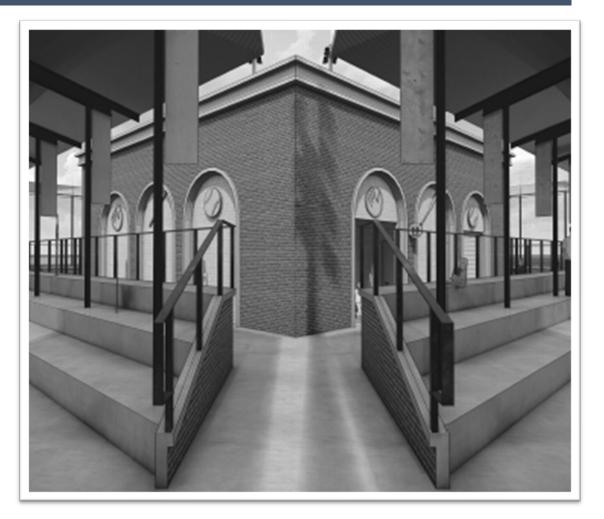



### **CENTRAL PARK OPERATIONS SHOP**



### Scope

Demolition and re-construction of the Operations Shop at Central Park to inlcude secure storage, workshops, restrooms and office space.

### Budget


\$7.4M

### Update

50% drawings submitted and are under review by various City Departments.

### Schedule

Estimated construction to start Spring of 2024.

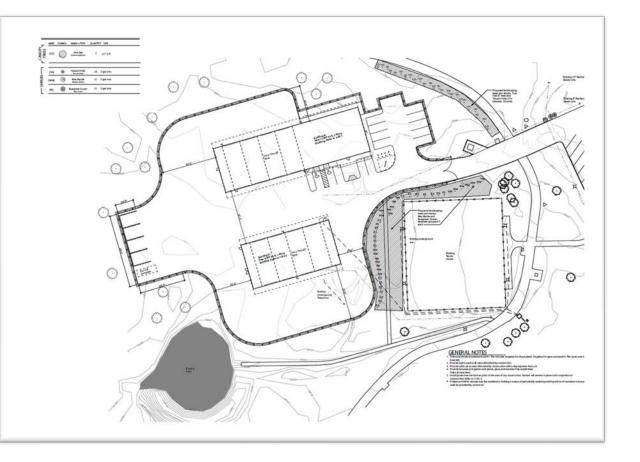



### **PICKLEBALL/FUTSAL COURTS**

### Scope

Installation of outdoor courts for pickleball, futsal and other sports with full LED lighting, lines and surfacing. Project may also include additional parking.

### **Budget**


\$1.7M

### Update

Public meeting held in July, finalizing multi-purpose court layout and components

#### Schedule

Anticipate construction start in 2024

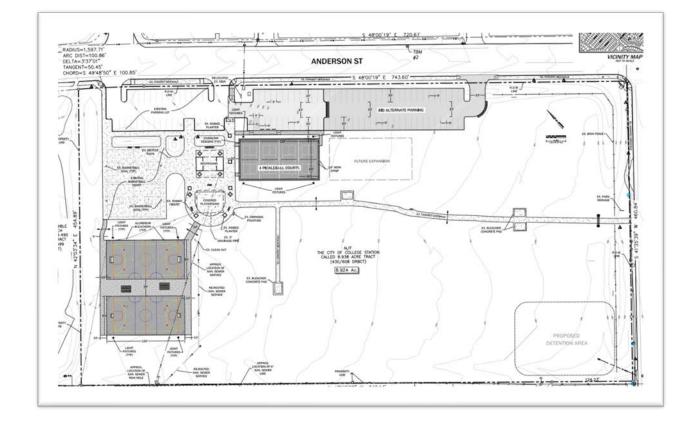

2022 Bond



### THOMAS PARK IMPROVEMENTS



#### Scope

Project will enhance Mabel Clare Thomas Park and maintain its existing character for a wide range of ages and a more diverse and active community.

### Budget

\$3M

**Update** Design team working on 30% design deliverables

Schedule Construction to start in 2025





### LINCOLN CENTER AREA IMPROVEMENTS

### Scope

Addition of bathrooms and pedestrian improvements

### Budget

\$1.2M

### Update

In conceptual design, finalizing location

### Schedule

Construction to start in 2024



**KEY LEGEND:** 

PROPOSED RESTROOM MOVE EXISTING FENCE BACKWARDS EXISTING SHADE TREES CONVERT 3 SPACES TO ACCESSIBLE PARKING SPACES TO ACCESSIBLE 2022

Bond



### **CITY HALL FLAG POLES**

### Scope

Add 4 flag poles with lighting to the front of City Hall

### **Budget**


Approx. \$40,000

### Update

Flag poles have been ordered.

### Schedule

Anticipate installation to begin in December

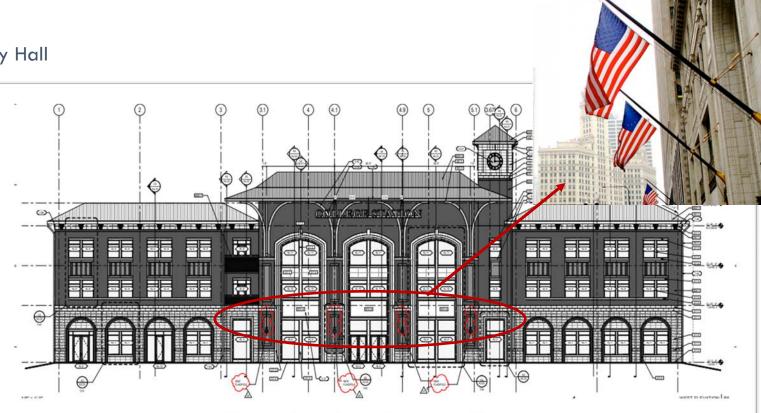



### FIRE STATION #7



### Scope

Design and Construction of Fire Station #7 along with site improvements. The Fire Station will be located south of the intersection of Dalton Dr. and Greens Prairie Rd.

### **Budget**

\$18M

### Update

Procuring design services, anticpate contract to Council December 2023

### Schedule

Anticipating project substantial completion by Fall 2026



2022 Bond

## QUESTIONS?

